Final bill

Recorded on:-

Work Code:- ND:002-18-000034

M. A. R. 57 (Rule 116)

Measurement Book

No. B Est Cost:- 25.00 Lakh

Work order No:- EE (YNK-D) E-PMT-02/W.O/74/2018-19

Serial No. 466618

Name of Work Improvements to drains at Syggappa layout and Surrounding areas in Ward No-02 of Yelahanka Sub division.

From ... To ...

Name of Contractor of nature of Agency Sri. Prakash Naik, No-313, Veerannapalya, Arabic College Post, Bangalore.

Date of commencement of work ...

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
1	KSRB 2-2.1: Earth work excavation for foundation of buildings, culverts water supply, Sanitary line and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5m in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead up to 50m, after breaking of clods Complete as per Specifications and directions of engineer in charge work.						
	Quantity vide, As per pre measurement are recorded						

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B

466625

No. .....
of Work ..... From..... To.....
of Contractor of nature of Agency .....
f commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
	1	13.90	0.75	-	10.42	
	1	1.80	0.75	-	1.35	
School Road :- H/s :-	80	0.75	0.60	-	36.00	
R/s :-	65	0.75	0.60	-	29.25	
					348.11 m^2	
Checked 12/12/18 AE-02	Limited to Schedule B' qty :-				348.00 m^2	7,60032.00
	CRS.				2184.00	
Providing and fixing Rcc pre cast slabs of 0.20 mm thick of cc 1:2:4 with 20mm and down size graded granite						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Ref. to Measurement No.
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	
	metal, machine mixed, including Cost of all materials labour, Hire of machinery, curing Complete as per specification and directions of engineer in charge work.						
	Precast slabs :- (200 mm Thick)						
	NES office Road :-	15	1.50	0.60	-	13.50	
	Kondappa Layout 15th Cross :-	5	1.50	0.60	-	4.50	
						18.00 m²	80.00
					@ RS.	4450.00	
	Total Bill Amount RS=25,94						

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zone)
Yelahanka, Bangalore

12/12/18
AE-02

Scanned by CamScanner

M. A. R. 57 (Rule 116)
Measurement Book

No. B

466626

No. .....
of Work ..... From..... To.....
of Contractor of nature of Agency .....
f commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8

CERTIFICATE:-

① Certified that the above work done is Satisfactory. Completed.

② Certified that the, there is no debries have been cleared to site.

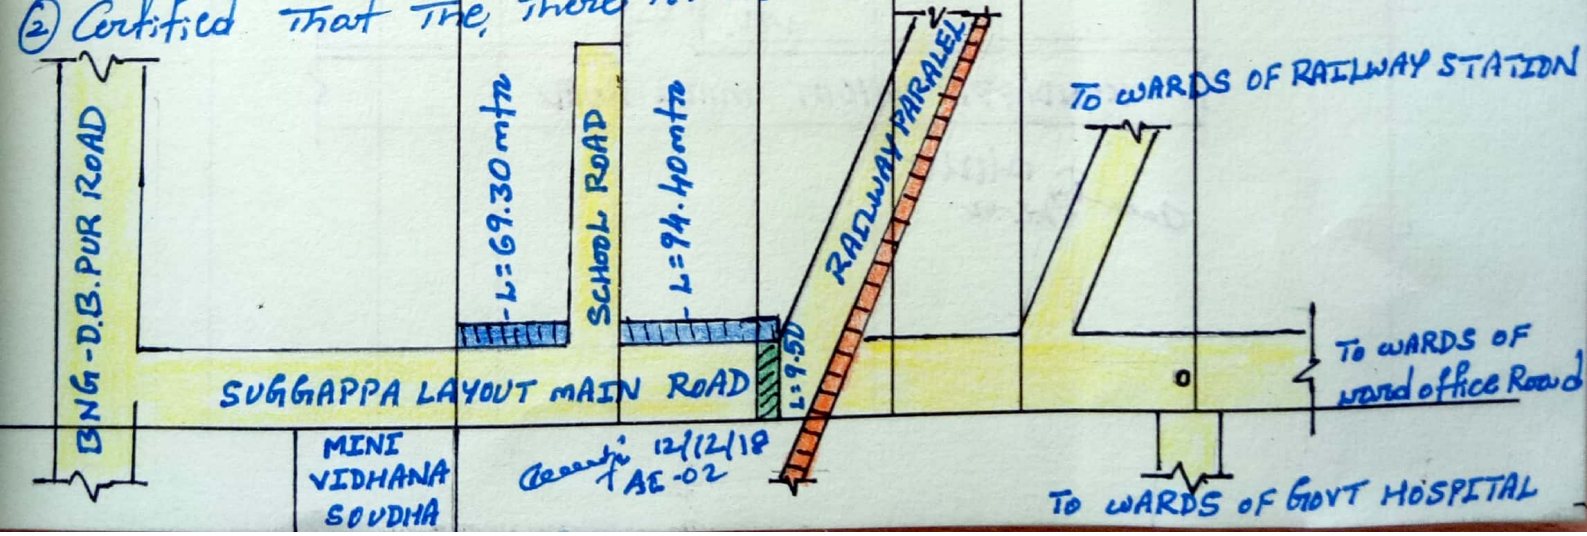

Scanned by CamScanner
